

Rancho Santiago Community College District Weekly Construction Update

October 17, 2013

Perimeter Site Improvements

Phase 1 - 5

Architect:	W+W Architects and Planners
Construction Manager:	Bernards
Contractor:	Woodcliff Corporation
Contract Start:	December 05, 2012
Contract Completion:	December 31, 2013

Anticipated Milestone Activities: Phase 4 10.21.13 – Parking Lot 7 Concrete Curbs 10.25.13 – CMU Wall Installation 10.28.13 – Parking Lot 7 Asphalt Paving

Scope: New asphalt paving, curbs, gutters and concrete paver drive entrances will be constructed to enhance the traffic flow throughout the Campus. Boarding the property; masonry walls and pilasters with decorative tile insets will be installed. Illuminated 'Santa Ana College' signage will be mounted on the masonry walls at various entrances to the College. New site lighting, irrigation and landscaping will complete the design.

Traffic Alert:

- Parking Lot 7 approx. 111 parking stalls will be unavailable due to upcoming construction activities associated with Phase 4.
- Use caution when existing via Bristol St., as crews are working along the curb line.
- Pacific Entrance (off Washington Ave.) will be closed from 7:00am 4:00pm PST. OCTA has been informed and bus service will be re-routed accordingly.

Status: Phase 1, 2 and 3 of this project is nearing completion and has been opened for access to vehicles and pedestrians. Recent activities for each phase of construction have been listed below:

- Phase 2 CMU Installation for Directional Signage
- Phase 3 CMU Installation for Directional Signage
- Phase 3 Slurry / Stripe New Asphalt
- Phase 3 Re-installation of Campus Directory
- Phase 4 CMU Wall Construction
- Phase 4 Parking Lot 7 Islands Pour
- Phase 4 Parking Lot 7 Curb Pour
- Phase 4 Parking Lot 7 Underground Electrical
- Phase 4 Irrigation
- Phase 4 Landscaping







Rancho Santiago Community College District Weekly Construction Update October 17, 2013







Rancho Santiago Community College District Weekly Construction Update

October 17, 2013

Building G Misc. Upgrades

Bldg G Misc. Upgrades

Architect: **Construction Manager: Contractor: Contract Start: Contract Completion:**

IBI Group, Inc. Bernards Optima RPM, Inc. May 27, 2013 September 14, 2013

Anticipated Milestone Activities:

Scope: Building G Miscellaneous Upgrades encompass work in and around the existing gymnasium built in 1954. The exterior work consist of new monumental stair at the north side of the building leading to a new storefront entrance, exterior lighting upgrade, concrete flat work, replacing of doors and windows in addition to some door hardware upgrades. Interior work includes two classroom renovations.

Traffic Alerts:

None noted.

Status: The recent construction activities are listed below:

Punch List Completion Work

This concludes the weekly construction updates for the above referenced project.
















Rancho Santiago Community College District Weekly Construction Update

October 17, 2013

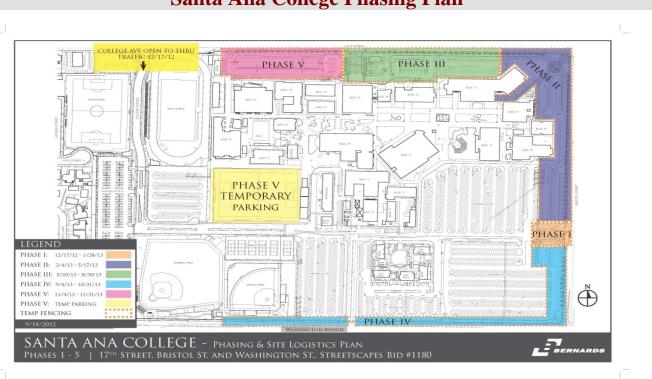

Santa Ana College Phasing Plan

Phase 1-5

Perimeter Site Improvements
